

# Status of Projects

Architecture, Engineering & Construction



# Objective

Update the GSD Board and Superintendency on the progress of major construction projects overseen by the Architecture, Engineering & Construction Department on behalf of Granite School District.



# Security Upgrades



# Security Upgrades Timeline

## SECURITY UPGRADES/REMODELS

Completed						In Progress			Pending			Future	
Prec.	School	Year	Prec.	School	Year	Prec.	School	Year	Prec.	School	Year	Prec.	School
1	Crestview El	2015	4	Vista El	2018	1	Eastwood El	2021	5	Valley Crest El	2022	1	Churchill Jr
1	Upland Terrace	2015	5	Farnsworth El	2018	1	Oakridge El	2021	6	Western Hills El	2022	1	Olympus Jr
2	Moss El	2015	5	Hillsdale El	2018	5	West Valley El	2021	6	West Kearns El	2022	1	Wasatch Jr.
3	Granger El	2015	6	Hunter El	2018	5	Wright El	2021	7	Silver Hills El	2022	1	Olympus High
3	Wilson El	2015	6	Oquirrh Hills El	2018	6	Frost El	2021				2	Cottonwood High
4	Bridger El	2015	6	Arcadia El	2018	7	Whittier El	2021				2	Granite Peaks
4	Plymouth El	2015	6	Valley Jr	2018	1	Skyline High	2024				2	Bonneville Jr
5	Jackling El	2015	7	Bacchus El	2018	7	Cyprus High	2025				3	Eisenhower Jr
5	Redwood El	2015	7	Copper Hills El	2018							4	Westbrook El
6	Academy Park El	2015	1	Driggs El	2019	1	Oakwood El	2022				4	Bennion Jr
6	Gourley El	2015	1	Rosecrest El	2019	1	Wm Penn El	2022				4	Kearns High
7	Magna El	2015	2	Spring Lane El	2019	2	Hartvigsen	2022				4	Taylorville High
7	Pleasant Green El	2016	4	Bennion El	2019	2	Woodstock El	2022				5	Granger High
1	Cottonwood El	2016	7	Diamond Ridge El	2019	5	Rolling Meadows El	2022				6	Kearns Jr
2	Roosevelt El	2016	7	Orchard El	2019	5	West Lake Jr	2024				6	Kennedy Jr
2	Twin Peaks El	2016	4	Beehive El	2020							6	Sandburg El
3	Taylorville El	2016	5	Armstrong Ac	2020							7	Brockbank Jr
5	Monroe El	2016	5	Pioneer El	2020							7	Hunter Jr
7	Hillside El	2018	7	Elk Run El	2020							7	Jefferson Jr
1	Morningside El	2018	7	Lake Ridge El	2020							7	Matheson Jr
1	Evergreen Jr	2018	3	Granite Park Jr.	2020							7	Hunter High
2	Lincoln El	2018	4	South Kearns El	2020								Jones Center
2	Mill Creek El	2018	0	Olene Walker El	2020								
3	Fremont El	2018	5	Stansbury El	2021								
4	Fox Hills El	2018	6	Truman El	2021								
4	Smith El	2018											

Elementary
Jr. High
High School



# Robert Frost Elementary

Security Remodel / Addition



Project is 100% complete.

Security remodel added approximately 700 square feet to the front of the school.

Interior was updated so patrons enter the front office to be checked in before gaining access to the building.

A new principal's office and a new conference room were created.

Upgraded the fire alarm system.

# Frost Exterior and Interior



# West Valley Elementary

## Security Remodel

Project is 75% complete.

Anticipated completion 10/16/2021.

Exterior work and landscaping complete.

Interior equipment and furnishings in place.

Final inspections pending.

Interior was updated so patrons enter the front office to be checked in before gaining access to the building.



# West Valley Exterior and Interior





# Gearld Wright Elementary

Security Remodel

Project is 99% complete.

Waiting on backordered ADA actuators.

Office staff are utilizing remodeled spaces.

Interior was updated so patrons enter the front office to be checked in before gaining access to the building.



# Wright Exterior and Interior



# Whittier Elementary

## Security Remodel

Project is 99% complete.

Waiting on backordered ADA actuators.

Office staff are utilizing remodeled spaces.

Interior was updated so patrons enter the front office to be checked in before gaining access to the building.



# Whittier Exterior and Interior



# Eastwood Elementary

## Security Remodel

Interior is 100% complete.

Waiting on backordered handrails to be installed outside the school.

Office staff are utilizing remodeled spaces.

Interior was updated so patrons enter the front office to be checked in before gaining access to the building.





# Eastwood Exterior and Interior



# Oakridge Elementary

Security Remodel / Addition



Project is 80% complete.

Anticipated completion is 11/15/2021.

Office staff are utilizing interior space.

Interior was updated so patrons enter the front office to be checked in before gaining access to the building.

Elevator installation began 09/29/2021.

Enclosure of ADA accessible entrance tower is in progress.

New sidewalk has been placed.

# Oakridge Exterior and Interior





# Campus Expansions



# West Lake Junior High School STEM (Westbrook Campus)

FACS Modular Building

Building is 100% complete.

Backordered furniture is shipping  
as available.



# West Lake FACS Modular Building



# Taylorville High School

Relocatable Classroom  
Complex

Building is 100% complete.

Backordered furniture is shipping  
as available.



# Taylorville Classroom Complex



# Infrastructure Replacement



# Cottonwood High School

## Track Reconstruction

Project is 85% complete.

Estimated finish date is 10/23/2021.

Asphalt and track surface have been replaced.

Drainage issues have been resolved.

Overgrowth has been removed.

New landscaping of curbing, rock, trees, irrigation, and fescue grass is in progress.



# Cottonwood Track





# Thomas Jefferson Junior High School

Chiller Upgrade

Project is 99% complete.

Punchlist items are in review.

Old cooling towers have been replaced with a 2-story enclosed structure containing the new chiller, pumps, and cooling tower.

School logo plaque still to be added to face of building.



# Jefferson Chiller Upgrade



# New Construction



# Skyline High School

Athletics Complex

Athletics phase is 60% complete.

Baseball diamond and football stadium are complete.

Interior painting is in progress.

Excavation for the pool is scheduled to begin in October.

Grading is underway for the athletic fields.



# Skyline Campus & Pool



# Cyprus High School

## Site Preparation

Site preparation is 100% complete.

Mass grading has been completed.

Kennecott site storm water  
drainage redirection project is  
completed.





# Cyprus Site Work



# Cyprus High School

Building Construction

Purchase order was issued to Westland Construction for construction of the new Cyprus High School.

Notice to proceed issued 09/13/2021.

Excavation of footings has begun.





# Cyprus Footings



# West Lake STEM Junior High School

Abatement / Demolition

Building abatement is 100% complete.

Demolition is at 40%, with completion scheduled for mid-November.

Classroom wings have been demolished and debris hauled away.

Demolition of the auditorium and gymnasium is on-going.



# West Lake Demolition



# West Lake STEM Junior High School

Replacement

Estimated project completion is 2024.

Design is in process with bidding in December 2021.

New West Lake is based on existing Utah middle school buildings using 21<sup>st</sup> century design with flexibility to support current and future learning activities.






# Preliminary West Lake Floor Plan



Sample Floor Plan (First Floor)

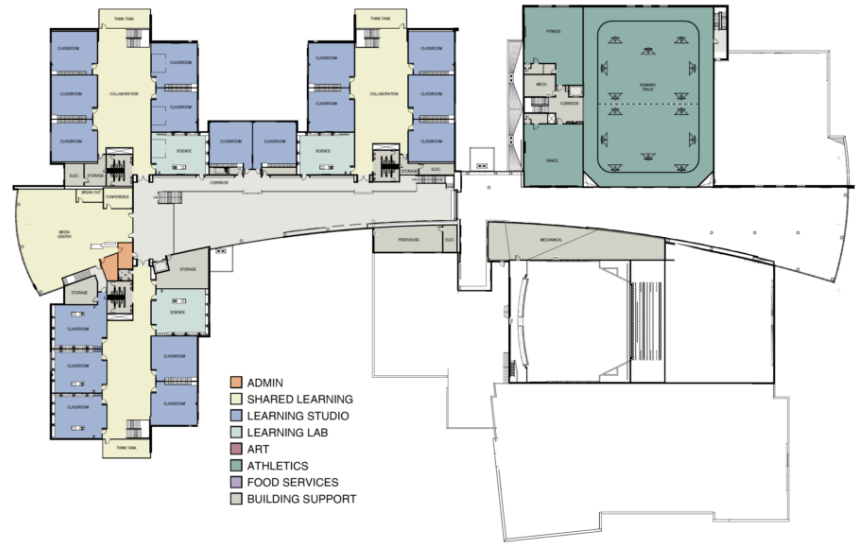

Sample Floor Plan (Second Floor)

